


Cost Summary by Task Type

Task Type		Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Overhead Cost	Total Cost	%
Bridges	Bridges	12.0	\$218.16	\$733.80	\$0.00	\$0.00	\$0.00	\$951.96	0.3%
Drain	Drainage	459.3	\$7,672.52	\$22,615.09	\$19,965.53	\$0.00	\$0.00	\$50,253.14	16.9%
Driveway	Driveway Work	83.0	\$1,544.06	\$3,445.20	\$1,087.20	\$0.00	\$0.00	\$6,076.46	2.0%
ROW	Right-of-way	895.5	\$15,927.11	\$61,547.15	\$0.00	\$0.00	\$0.00	\$77,474.22	26.1%
Roads	Roads	1,415.0	\$22,611.59	\$51,618.11	\$87,957.53	\$0.00	\$0.00	\$162,187.12	54.5%
Signs	Signs	13.0	\$243.22	\$98.40	\$117.07	\$0.00	\$0.00	\$458.69	0.2%
Task Types:	6	2,877.8	\$48,216.66	\$140,057.75	\$109,127.33	\$0.00	\$0.00	\$297,401.58	

Cost Summary by Task Type

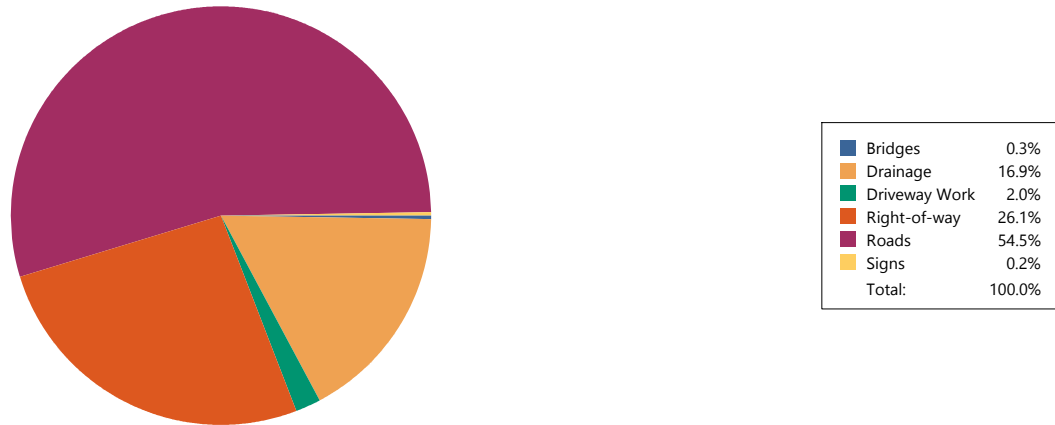

Task Performance by Location

315 Creekside St. (parkside)					1022
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/02/2019	12/02/2019	3	\$150.79	
Tasks:	1			\$150.79	
315 Hickory St. (parkside)					1023
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/02/2019	12/02/2019	3	\$150.79	
Tasks:	1			\$150.79	
315 Parkside St. (parkside)					1024
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/02/2019	12/02/2019	3	\$150.79	
Tasks:	1			\$150.79	
315 Poolside Dr. (parkside)					1025
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/02/2019	12/02/2019	3	\$150.79	
Tasks:	1			\$150.79	
Cr 4101 Perry (ext 4117)					1038
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/12/2019	12/12/2019	3	\$482.39	
Tasks:	1			\$482.39	
Cr 41107 Mill Run Rd (35 Mph)					1049
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cut Brush/ Brush Cutter	10/03/2019	10/24/2019	8	\$8,757.00	
Tasks:	1			\$8,757.00	
Cr 41126 Labello					1052
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Driveway entrance - repaired	10/23/2019	10/23/2019	2	\$1,089.34	
Other driveway work	10/16/2019	10/16/2019	2	\$102.68	
Tasks:	2			\$1,192.02	
Cr 4117 B.ville (minor Collector)					1053
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/12/2019	12/12/2019	3	\$482.39	
Remove Damaged Tree	11/27/2019	11/27/2019	3	\$1,278.74	

Task Performance by Location

Tasks:	2				\$1,761.13
Cr 41511 (larry Anding)					1060
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cut Brush/ Brush Cutter	10/29/2019	10/31/2019	3	\$3,356.85	
Tasks:	1				\$3,356.85
Cr 41512 Ryan					1062
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cut Brush/ Brush Cutter	11/01/2019	11/21/2019	5	\$4,524.45	
Tasks:	1				\$4,524.45
Cr 41513					1063
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cut Brush/ Brush Cutter	12/12/2019	12/12/2019	1	\$146.40	
Tasks:	1				\$146.40
Cr 41514					1064
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cut Brush/ Brush Cutter	12/02/2019	12/11/2019	4	\$3,065.40	
Other drainage work	12/13/2019	12/13/2019	2	\$493.98	
Tasks:	2				\$3,559.38
Cr 4201 Sunrise (off 315) (minor Collector)					1069
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Remove Dead Tree	11/15/2019	11/15/2019	2	\$555.90	
Tasks:	1				\$555.90
Cr 4213 Twin Oaks (off Fm 315)					1079
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/02/2019	12/02/2019	3	\$150.79	
Tasks:	1				\$150.79
Cr 4215 Welder (ext 4224)					1083
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Other sign work	11/01/2019	11/01/2019	1	\$49.46	
Tasks:	1				\$49.46
Cr 4217 Manoy (pleasant Ridge)					6004
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	

Task Performance by Location

Bladed - add water	10/09/2019	10/09/2019	3	\$1,262.76
Grind Road (Bomag Reclaimer)	10/08/2019	10/08/2019	4	\$1,518.30
Mix CKD	10/31/2019	11/01/2019	9	\$7,771.18
Stabilized ditch erosion	10/07/2019	10/08/2019	8	\$2,303.42

Tasks: 4 \$12,855.66

Cr 4222 Kennedy Corner (45 Mph) 1086

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	10/22/2019	10/22/2019	4	\$123.98
Mow Right-of-Way	10/01/2019	10/01/2019	1	\$50.13
Patched - road surface	10/23/2019	10/23/2019	3	\$275.90

Tasks: 3 \$450.01

Cr 4224 Stella Walker (45 Mph) 1087

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	10/22/2019	10/22/2019	4	\$771.91
Mow Right-of-Way	10/01/2019	10/01/2019	1	\$50.13
Other sign work	11/01/2019	11/01/2019	1	\$49.46
Patched - road surface	10/22/2019	10/24/2019	9	\$804.61
Remove Dead Tree	11/15/2019	11/15/2019	2	\$555.90

Tasks: 5 \$2,232.01

Cr 4225 Red Flat (45 Mph) 1088

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Mow Right-of-Way	10/01/2019	10/01/2019	1	\$50.13
Other sign work	11/01/2019	11/01/2019	1	\$49.46
Patched - road surface	10/22/2019	10/23/2019	6	\$503.04
Put up County road number sign	11/01/2019	11/01/2019	1	\$33.30

Tasks: 4 \$635.93

Cr 4228 Bruno 1090

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/24/2019	10/24/2019	3	\$301.57

Tasks: 1 \$301.57

Cr 4231 Bethel Cemetary 1092

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Mow Right-of-Way	10/02/2019	10/02/2019	1	\$37.60
Patched - road surface	12/09/2019	12/09/2019	3	\$974.79

Tasks: 2 \$1,012.39

Cr 4233 Newman (ext 4235) 1093

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/22/2019	10/22/2019	3	\$227.14

Task Performance by Location

Tasks:	1				\$227.14
Cr 4234 (Bristow Addition)					1094
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Bladed - road surface	11/19/2019	11/19/2019	2		\$680.08
Tasks:	1				\$680.08
Cr 4235 Johns (35 Mph)					1095
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Oil Sand Overlay	12/06/2019	12/06/2019	5		\$2,584.32
Patched - road surface	10/18/2019	10/22/2019	6		\$525.50
Road surface repair	12/06/2019	12/06/2019	8		\$3,016.08
Tasks:	3				\$6,125.90
Cr 4236 Dansby (ext 4235)					1096
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Oil Sand Overlay	12/05/2019	12/05/2019	5		\$10,462.18
Other road work	12/04/2019	12/04/2019	2		\$205.36
Patched - road surface	10/18/2019	10/22/2019	6		\$525.50
Tasks:	3				\$11,193.04
Cr 4303 Gene Linsey (off 314)					1104
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	10/08/2019	10/09/2019	2		\$1,705.01
Tasks:	1				\$1,705.01
Cr 4304 Lone Star (off Fm 314)					9001
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	10/09/2019	11/18/2019	13		\$10,096.15
Road culvert - installed	12/23/2019	12/23/2019	2		\$870.84
Road surface repair	11/18/2019	11/18/2019	15		\$4,513.42
Tasks:	3				\$15,480.41
Cr 4305n C. Harmon (ext 4304)					1105a
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	12/02/2019	12/16/2019	5		\$4,615.40
Tasks:	1				\$4,615.40
Cr 4305s Hightower (ext 4304)					1105
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	11/19/2019	11/21/2019	3		\$2,524.04

Task Performance by Location

Tasks:	1				\$2,524.04
Cr 4307 Gussie Lee (35 Mph) {minor Collector}					1106
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Mow Right-of-Way	10/02/2019	10/02/2019	1		\$37.60
Tasks:	1				\$37.60
Cr 4308 Steve (off 4305 N)					1107
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	11/22/2019	11/26/2019	2		\$1,504.12
Tasks:	1				\$1,504.12
Cr 4309 Live Cove (off 4307)					9003
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	10/03/2019	10/07/2019	3		\$1,905.91
Mow Right-of-Way	10/02/2019	10/02/2019	1		\$37.60
Patched - road surface	10/02/2019	10/02/2019	3		\$251.87
Tasks:	3				\$2,195.38
Cr 4317a Moore Sta. Loop					9004
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	10/01/2019	10/03/2019	3		\$1,555.64
Mow Right-of-Way	10/02/2019	10/02/2019	1		\$37.60
Tasks:	2				\$1,593.24
Cr 4317b Hoe Handle					1115
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Bladed - add millings	12/09/2019	12/09/2019	3		\$424.96
Tasks:	1				\$424.96
Cr 4319 Feds (minor Collector)					1117
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cut Brush/ Brush Cutter	12/17/2019	12/17/2019	1		\$803.58
Patched - road surface	10/02/2019	10/02/2019	3		\$251.87
Tasks:	2				\$1,055.45
Cr 4321 Presswood					1119
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Bladed - add millings	12/19/2019	12/19/2019	2		\$1,464.96
Cleared debris or fallen tree	12/26/2019	12/26/2019	3		\$2,000.64
Tasks:	2				\$3,465.60

Task Performance by Location

Cr 4322 Tip Top					1120
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patched - road surface	12/06/2019	12/06/2019	3	\$879.31	
Tasks:	1				\$879.31

Cr 4325 N.y.- Moore Station (minor Collector)					1123
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cleared debris or fallen tree	10/14/2019	10/14/2019	1	\$61.76	
Mow Right-of-Way	10/07/2019	10/08/2019	2	\$1,925.92	
Remove Damaged Tree	10/16/2019	10/16/2019	5	\$385.11	
Road surface repair	11/19/2019	11/19/2019	2	\$680.08	
Tasks:	4				\$3,052.87

Cr 4328 Zip Line (35 Mph)					1126
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cleared debris or fallen tree	10/21/2019	10/21/2019	3	\$418.00	
Tasks:	1				\$418.00

Cr 4329 (off 4325)					1127
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Mow Right-of-Way	10/04/2019	10/04/2019	1	\$966.96	
Tasks:	1				\$966.96

Cr 4330 Dingler					1128
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Patch- FALL IN	12/27/2019	12/27/2019	3	\$430.12	
Remove Low Hanging Limb	10/23/2019	10/23/2019	3	\$451.78	
Tasks:	2				\$881.90

Cr 4331 Terrell-Howeth					1129
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Mow Right-of-Way	10/09/2019	10/10/2019	2	\$1,326.57	
Tasks:	1				\$1,326.57

Cr 4334 N.y. Church					1131
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost	
Cleared debris or fallen tree	10/09/2019	10/21/2019	5	\$665.80	
Mow Right-of-Way	10/03/2019	10/03/2019	1	\$958.96	
Patched - road surface	11/18/2019	11/18/2019	3	\$249.86	
Tasks:	3				\$1,874.62

Cr 4335 Archie Dennis-A (ext 4334)					1132
---	--	--	--	--	-------------

Task Performance by Location

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cut Brush/ Brush Cutter	10/14/2019	10/14/2019	1	\$73.20
Tasks: 1				\$73.20
Cr 4336 Myrtle Springs (45 Mph)				1133
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	10/21/2019	10/21/2019	3	\$418.00
Driveway culvert - installed/set	12/09/2019	12/09/2019	4	\$1,156.96
Driveway entrance - repaired	12/13/2019	12/13/2019	2	\$493.98
Mow Right-of-Way	10/01/2019	10/02/2019	2	\$1,340.04
Other driveway work	12/02/2019	12/02/2019	1	\$49.71
Patched - road surface	11/19/2019	11/20/2019	5	\$878.03
Tasks: 6				\$4,336.72
Cr 4341 Taylor Farms Rd (ext 4336)				1137
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Bladed - road surface	11/08/2019	11/08/2019	2	\$1,464.96
Tasks: 1				\$1,464.96
Cr 4344 Bob Walker				1139
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Bladed - add millings	11/13/2019	11/13/2019	4	\$1,365.84
Cleared debris or fallen tree	10/21/2019	10/21/2019	4	\$540.16
Patched - road surface	10/24/2019	10/24/2019	3	\$301.57
Tasks: 3				\$2,207.57
Cr 4346 Smith				1141
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Bladed - add millings	11/13/2019	11/13/2019	4	\$441.20
Mow Right-of-Way	10/02/2019	10/02/2019	1	\$479.48
Tasks: 2				\$920.68
Cr 4348 Sholars				1142
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Road Cuvert (mark for dig tess)	12/26/2019	12/26/2019	1	\$8.15
Tasks: 1				\$8.15
Cr 4350 Larue Cemetary				1144
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cut Brush/ Brush Cutter	10/14/2019	10/14/2019	1	\$73.20
Remove Dead Tree	10/15/2019	10/16/2019	9	\$1,990.40
Tasks: 2				\$2,063.60

Henderson County Pct. 4**Task Performance by Location**

Cr 4400 Rockhill (35 Mph)				1151
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Clean Culvert/Beaver Dam	10/25/2019	10/25/2019	3	\$173.86
Patched - road surface	10/07/2019	10/08/2019	6	\$598.16
Tasks:	2			\$772.02
Cr 4401 Douglas Loop				1152
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Clean Culvert/Beaver Dam	12/19/2019	12/19/2019	2	\$234.62
Stabilized ditch erosion	10/18/2019	10/18/2019	6	\$2,969.96
Tasks:	2			\$3,204.58
Cr 4403 Sissys				1154
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Clean Culvert/Beaver Dam	10/15/2019	12/19/2019	7	\$1,220.82
Patched - road surface	11/20/2019	12/03/2019	5	\$881.50
Stabilized ditch erosion	10/25/2019	10/25/2019	3	\$552.58
Tasks:	3			\$2,654.90
Cr 4501 Country Ln				1159
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/02/2019	10/02/2019	3	\$251.87
SET UP Barricades	11/07/2019	11/07/2019	2	\$102.68
Tasks:	2			\$354.55
Cr 4504 Rakestraw				1162
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Road surface repair	12/03/2019	12/03/2019	5	\$2,308.77
Tasks:	1			\$2,308.77
Cr 4509 Harry Mills				1166
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Remove Dead Tree	10/22/2019	10/22/2019	4	\$540.42
Tasks:	1			\$540.42
Cr 4510				1167
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	12/05/2019	12/05/2019	3	\$430.03
Remove Low Hanging Limb	10/23/2019	10/23/2019	3	\$451.78
Road surface repair	12/03/2019	12/03/2019	5	\$1,190.52
Tasks:	3			\$2,072.33

Task Performance by Location

Cr 4511 Baxter/Pinegrove (45 Mph) (minor Collector)				1168
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Driveway culvert - reset	12/02/2019	12/02/2019	4	\$924.38
Patched - road surface	11/05/2019	11/05/2019	3	\$236.96
Tasks: 2				\$1,161.34
Cr 4515 Richardson (35 Mph)				1176
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Remove Low Hanging Limb	10/23/2019	10/23/2019	3	\$451.78
Replaced damaged/missing sign	12/12/2019	12/12/2019	1	\$43.23
Tasks: 2				\$495.01
Cr 4516 Hairgrove				1177
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Clean Culvert/Beaver Dam	10/15/2019	12/16/2019	4	\$1,136.08
Cleared debris or fallen tree	11/21/2019	11/21/2019	4	\$1,051.02
Patched - road surface	12/03/2019	12/03/2019	3	\$455.06
Tasks: 3				\$2,642.16
Cr 4518 Burnett / Super Cop (35mph)				1179
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Chip Brush w/ Wood Chipper	10/03/2019	10/03/2019	3	\$131.74
Tasks: 1				\$131.74
Cr 4520e Rainbow-E (Rainbo Gate To 4402				1180
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Chip Brush w/ Wood Chipper	12/30/2019	12/30/2019	3	\$1,139.52
Cleared debris or fallen tree	12/12/2019	12/31/2019	11	\$3,993.96
Tasks: 2				\$5,133.48
Cr 4520w Rainbow-W (1615 To Rainbo Gate)				1181
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	12/31/2019	12/31/2019	5	\$957.07
Tasks: 1				\$957.07
Cr 4528 County Line (35 Mph)				1186
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/08/2019	12/02/2019	6	\$458.92
Tasks: 1				\$458.92
Cr 4538 Colonial Circle				1193

Task Performance by Location

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Other drainage work	10/02/2019	10/03/2019	6	\$350.59
Patched - road surface	10/07/2019	10/07/2019	3	\$290.03
Tasks: 2				\$640.62
Cr 4600 Carroll Springs (35 Mph)				1194
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	12/27/2019	12/27/2019	3	\$1,004.72
Patched - road surface	11/18/2019	11/18/2019	3	\$249.86
Tasks: 2				\$1,254.58
Cr 4604 Terry Davis				1197
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Driveway entrance - repaired	10/23/2019	10/23/2019	2	\$789.34
Patched - road surface	11/18/2019	11/18/2019	3	\$249.86
Tasks: 2				\$1,039.20
Cr 4608 D Warren				1199
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Put up SPEED LIMIT sign NS	11/07/2019	11/07/2019	4	\$141.14
Tasks: 1				\$141.14
Cr 4610 Gary Rd				1200
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Other bridge work	11/08/2019	11/08/2019	2	\$951.96
Other road work	11/14/2019	11/14/2019	2	\$1,257.52
Road culvert - installed	11/05/2019	11/20/2019	18	\$28,965.01
Road culvert - replaced	11/04/2019	11/22/2019	14	\$5,360.57
Stabilized ditch erosion	11/12/2019	11/15/2019	9	\$5,075.44
Tasks: 5				\$41,610.50
Cr 4612 Mays Café				1205
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cut Brush/ Brush Cutter	10/01/2019	10/01/2019	1	\$146.40
Tasks: 1				\$146.40
Cr 4613 Old 19 (35 Mph)				1206
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	12/05/2019	12/05/2019	3	\$430.03
Tasks: 1				\$430.03
Cr 4614 Holder (35 Mph)				1207

Task Performance by Location

Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Cleared debris or fallen tree	10/21/2019	10/21/2019	4	\$540.16
Tasks: 1				\$540.16
Cr 4627 Gibson (minor Collector)				1217
Patched - road surface	11/01/2019	11/01/2019	3	\$455.48
Tasks: 1				\$455.48
Cr 4700 Ward (35 Mph) (minor Collector)				1219
Patched - road surface	11/05/2019	11/05/2019	3	\$236.96
Tasks: 1				\$236.96
Cr 4704 Ray Road				1224
Driveway culvert - installed/set	12/17/2019	12/17/2019	3	\$1,438.03
Tasks: 1				\$1,438.03
Cr 4705 Thomas Frank				1225
Other driveway work	12/11/2019	12/11/2019	1	\$32.04
Tasks: 1				\$32.04
Cr 4715 Alligator				1232
Patched - road surface	11/19/2019	11/19/2019	3	\$451.59
Tasks: 1				\$451.59
Cr 4718 Hallmark				1235
Patched - road surface	11/05/2019	11/18/2019	6	\$486.82
Tasks: 1				\$486.82
Cr 4720 Lambright				1237
Mow Right-of-Way	10/14/2019	10/14/2019	1	\$958.96
Tasks: 1				\$958.96

Task Performance by Location

Cr 4800 Baxter Rd (45 Mph) (minor Collector)				1238
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	11/01/2019	11/05/2019	6	\$692.44
Remove Dead Tree	10/16/2019	10/16/2019	5	\$352.21
Tasks: 2				\$1,044.65
Cr 4815 Suncrestdr. (off 2495)				1267
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Other sign work	12/12/2019	12/12/2019	1	\$92.64
Tasks: 1				\$92.64
Cr 4825 Bearcreek (minor Collector)				1272
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/01/2019	10/01/2019	3	\$305.42
Tasks: 1				\$305.42
Cr 4825a Bearcreek Circle				1273
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/01/2019	10/01/2019	3	\$305.42
Tasks: 1				\$305.42
Cr 4826 Hopson				1274
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Patched - road surface	10/01/2019	10/01/2019	3	\$305.42
Tasks: 1				\$305.42
Cr 4828 Rounsavall				1277
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Remove Damaged Tree	11/12/2019	11/12/2019	2	\$491.79
Tasks: 1				\$491.79
Cr 4833 John Mark				1282
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Oil Sand Overlay	11/06/2019	11/06/2019	4	\$9,135.43
Tasks: 1				\$9,135.43
Cr 4835 Coleman				1284
Task	Earliest Date	Most Recent Date	Crew Size	Total Cost
Oil Sand Overlay	11/04/2019	11/05/2019	14	\$22,065.08
Other road work	11/07/2019	11/07/2019	1	\$680.96

Task Performance by Location

Tasks:	2				\$22,746.04
Cr 4838 Garner					1287
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cleared debris or fallen tree	12/23/2019	12/23/2019	2		\$504.84
Tasks:	1				\$504.84
Cr 4908 Joe Browning					1290
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Cleared debris or fallen tree	10/21/2019	10/21/2019	4		\$540.16
Tasks:	1				\$540.16
Cr 4912 Crystal					1293
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Asphalt overlay	10/28/2019	10/28/2019	11		\$23,719.22
Tasks:	1				\$23,719.22
Cr 4913 Dusty Rd.					1294
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Asphalt overlay	10/28/2019	10/29/2019	18		\$25,086.08
Cleared debris or fallen tree	12/11/2019	12/11/2019	4		\$1,994.54
Tasks:	2				\$27,080.62
Elm Street					8007
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Bladed - add water	10/03/2019	10/07/2019	8		\$2,755.92
Grind Road (Bomag Reclaimer)	10/01/2019	10/01/2019	3		\$2,296.32
Mix CKD	10/02/2019	10/02/2019	5		\$6,365.86
Oil Sand Overlay	10/10/2019	10/17/2019	18		\$9,589.63
Road culvert - Stabilize	10/04/2019	10/04/2019	4		\$537.22
Tasks:	5				\$21,544.95
Lee Street					8010
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Patched - road surface	10/17/2019	10/17/2019	3		\$406.77
Tasks:	1				\$406.77
Pct 4 Barn					358
Task	Earliest Date	Most Recent Date	Crew Size		Total Cost
Material - stockpiled	12/18/2019	12/18/2019	1		\$499.44
Tasks:	1				\$499.44

Task Performance by Location

Total Cost

Grand Total

\$297,401.58
